verity



The same controlled chain. A sharper price.

The recalculated proposal for D & S Electric Works: re-priced module by module after a detailed product-management review, with the AI and automation layers that DSEW does not need to run its factory taken out of the fee.

PREPARED FOR

D & S Electric Works
109, Industrial Area Extension, Rau, Indore 453331

PREPARED BY

PlotArmour
team@plotarmour.in · +91 87440 69597

EDITION

Recalculated · 23 October 2026 · valid 60 days

SUPERSEDES

Prices and AI scope in document 1

CONFIDENTIAL DRAFT FOR FINAL REVIEW

Everything the factory runs on. Nothing it does not.

Our product managers re-examined every module line of the first proposal against how DSEW actually works: an engineered, one-off product traced from approved drawing to tested unit. The controlled chain, the quality gates and every module stay. The AI and automation layers that nothing in that chain depends on come out of the price, and the MVP's module and implementation lines are re-priced to what each costs to build.

OPTION 1 · MVP

₹2,40,000

9 modules, one connected core workflow. Was ₹3,25,000: ₹85,000 lower. About 6 to 8 weeks from kickoff.

OPTION 2 · COMPLETE ERP

₹3,80,000


All 18 operating modules of your enquiry. Was ₹4,80,000: ₹1,00,000 lower. About 8 to 12 weeks from kickoff.

TESTING PERIOD

₹8,500 /month

Unchanged: warranty, testing support and maintenance in one monthly fee, for as many months as DSEW chooses.

One-time licence and implementation fees, plus GST. Use for DSEW's own business, one site, up to 15 named users; no annual or per-user licence fee. Option 3 is the Complete ERP in four accepted phases at the same ₹3,80,000. Prices are fixed.

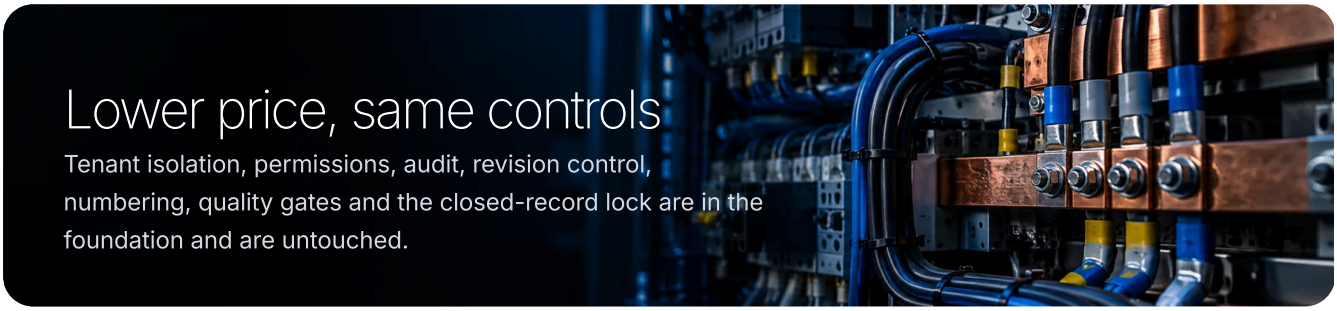

Lower price, same controls

Tenant isolation, permissions, audit, revision control, numbering, quality gates and the closed-record lock are in the foundation and are untouched.

01 What the review changed, to the rupee

Every reduction is named. The AI and automation lines are removals; the MVP's ₹40,000 is a re-pricing of its module and implementation lines with no scope taken out. Nothing was discounted by trimming a control, a module or a deliverable that DSEW's workflow needs.

REMOVAL	WHERE IT SAT	OPTION 1 (₹)	OPTION 2 (₹)
AI adapters (search, read and summarise layers, with their own configuration, access control and audit logging)	Inside the module lines	45,000	75,000
AI adapter layer in cross-module integration and deployment (adapter wiring, search index set-up)	Implementation line	included above	5,000
Documented AI use cases (module 19, with acceptance thresholds on sample documents)	Module line 19	not in Option 1	15,000
Workflow automation (escalations, cross-module triggers, automated document generation)	Module line 18	not in Option 1	5,000
Module and implementation re-pricing (MVP only; scope unchanged, see section 4)	Module lines 1 to 7, implementation lines	40,000	none
Total reduction		85,000	1,00,000
Previous total, ex GST		3,25,000	4,80,000
Recalculated total, ex GST		**2,40,000**	**3,80,000**

The first proposal stated the AI adaptability inside the module prices as about ₹40,000 to ₹50,000 (Option 1) and ₹80,000 to ₹90,000 (Option 2). The amounts removed, ₹45,000 and ₹80,000 (₹75,000 plus ₹5,000), sit inside those stated ranges.

Why the AI came out

An adapter is a connection point, not a model: it does nothing until DSEW also buys hardware or a service behind it. Search and summaries over a 15-user installation are not on the path of any quotation, BOM, job, traveller or test. Carrying them in every module line made each line dearer and the server heavier, for a benefit DSEW has not asked to use on day one.

Why the automation came out

Escalation chains, cross-module triggers and auto-generated documents are tuned to a factory's habits after it has run the workflows for a while. Approval workflows and reminders stay, so the controlled chain is complete; the tuned automation can follow once DSEW's own testing shows which rules are worth having.

02 What does not change

AREA	POSITION IN THIS EDITION
Modules	All 9 MVP modules and all 18 Complete ERP operating modules remain, at the same agreed baseline depth and with the same module-by-module acceptance criteria (section 6)

AREA	POSITION IN THIS EDITION
Controlled chain	Enquiry, quotation, order, project, engineering documents and BOM with revisions, material availability, manufacturing job, traveller, quality inspection and release, delivery readiness. A failed or missing mandatory check blocks release; a released revision cannot be edited; a closed record stays locked
Configurable, not hard-coded	Test templates, checklists, workflows and approvals, routes, roles and permissions, print formats, fields and forms, numbering, master data, notifications and module switches are set by DSEW's administrators on screen
Foundation	Tenant isolation, sign-in, the permission check, the audit trail, backup with a tested restore, data export in CSV with files and an index
Delivery	One DSEW Linux VM, testing and UAT, training, administrator and user guides, runbooks. Estimates stay about 6 to 8 weeks (Option 1) and about 8 to 12 weeks (Options 2 and 3) until the signed specification confirms them
Testing period	₹8,500 a month ex GST, from go-live, ended at the close of any monthly cycle; same warranty, testing assistance and maintenance; 8 hours a month included; same response targets
Payment, ownership, licence	Same four milestones (30, 30, 30, 10 percent) and 7-day terms; same ownership and licence position (document 3); same user, site and change-request rules

03 What is deferred, and how it comes back

Nothing is closed off. Each deferred capability can be added to the same workspace later by written change request, quoted on its own, against DSEW's real usage and a hardware decision taken with the cost in front of DSEW.

DEFERRED CAPABILITY	WHAT IT WOULD BE	DEPENDENCY WHEN ADDED
Search and summaries over records	Natural-language search across authorised documents, quotations, POs, BOMs and jobs, inside each user's permissions and audit	Index storage; a VM of about 4 to 6 vCPU and 32 GB memory
Document classification and gap detection	Metadata extraction, missing-document and incomplete-record flags (largely rules)	Accuracy proven on DSEW's sample documents
Drafting from approved templates	Quotations, work instructions, inspection plans and reports	A separate on-premises GPU workstation of about 16 GB, or an external service with per-use charges
Tuned workflow automation	Escalations, cross-module triggers, auto-generated documents	Rules DSEW has settled during its testing period

The foundation was built so that any of these can be added without redesign: every read and write already passes one permission gate and one audit trail, so an added capability inherits DSEW's access rules. AI would never be an approver, and no essential workflow would depend on it. The amounts removed in section 1 are not a promise of the price of the later work; each is quoted when asked for.

04 Option 1: MVP, recalculated

One connected workflow from customer enquiry to delivery readiness. Creating a manufacturing job identifies its BOM, shows material availability, records material issues, tracks operations and the traveller, and blocks final release while mandatory quality checks are incomplete.

#	MODULE / DELIVERABLE	PREVIOUS (₹)	RECALCULATED (₹, EX GST)	CHANGE
1	CRM, enquiry and quotation management	35,000	25,000	−10,000
2	Project and order management	25,000	15,000	−10,000
3	Document management and configurable numbering	35,000	25,000	−10,000
4	Basic engineering and BOM management	35,000	25,000	−10,000
5	Basic procurement and inventory management	40,000	30,000	−10,000
6	Manufacturing execution and job management	40,000	30,000	−10,000
7	Manufacturing traveller management	25,000	15,000	−10,000
8	Core quality management	30,000	25,000	−5,000
9	Operational dashboards and basic notifications	15,000	10,000	−5,000
	Module development subtotal	**2,80,000**	**2,00,000**	**−80,000**
	Requirements finalisation and workflow design	12,000	10,000	−2,000
	Application configuration and deployment	10,000	10,000	0
	Integrated testing and UAT support	12,000	10,000	−2,000
	Documentation, training and handover	11,000	10,000	−1,000
	Implementation subtotal	**45,000**	**40,000**	**−5,000**
	MVP total (ex GST)	**3,25,000**	**2,40,000**	**−85,000**

Each of the nine module lines carried one AI adapter, a uniform ₹5,000 integration layer (₹45,000 in all), so each falls by that amount. Modules 1 to 7 fall by a further ₹5,000 each (₹35,000) and the four implementation lines by ₹5,000 together, the ₹40,000 re-pricing in section 1; core quality and dashboards take only the AI reduction. No module, deliverable or acceptance criterion is removed by the re-pricing. The dashboards module keeps in-app reminders and operational dashboards; AI summaries are removed.

MVP boundary. Basic BOMs, material records, purchasing, stock balances and job-level material allocation are included. Excluded: advanced MRP, barcode-driven genealogy, finance and accounting, payroll and HR,

dispatch workflow, contracts and compliance tracking, any AI or AI adapter, workflow automation beyond basic reminders, and advanced enterprise workflows.

05 Option 2: Complete ERP, recalculated

#	MODULE / DELIVERABLE	PREVIOUS (₹)	RECALCULATED (₹, EX GST)	CHANGE
1	CRM, enquiry, quotation and sales order management	30,000	25,000	−5,000
2	Advanced project management	20,000	15,000	−5,000
3	Engineering and product lifecycle management	30,000	25,000	−5,000
4	Document management and controlled document workflows	25,000	20,000	−5,000
5	Manufacturing execution	30,000	25,000	−5,000
6	Manufacturing travellers and process documentation	15,000	10,000	−5,000
7	Quality management system	25,000	20,000	−5,000
8	Barcode, QR code and traceability	15,000	10,000	−5,000
9	Procurement and vendor management	20,000	15,000	−5,000
10	Inventory and warehouse management	20,000	15,000	−5,000
11	Production planning and basic MRP	20,000	15,000	−5,000
12	Testing and equipment management	15,000	10,000	−5,000
13	Finance and accounting, built inside Verity	20,000	15,000	−5,000
14	HR and payroll management	15,000	10,000	−5,000
15	Dispatch and logistics	10,000	10,000	0
16	Contracts, compliance and risk	10,000	10,000	0
17	Management dashboards and business intelligence	15,000	10,000	−5,000
18	Notifications and approval workflows RENAMED	15,000	10,000	−5,000
19	AI, documented use cases	15,000	removed	−15,000
	Module development subtotal	**3,65,000**	**2,70,000**	**−95,000**
	Requirements analysis and solution architecture	25,000	25,000	0

#	MODULE / DELIVERABLE	PREVIOUS (₹)	RECALCULATED (₹, EX GST)	CHANGE
	UI/UX design and workflow configuration	20,000	20,000	0
	Cross-module integration and deployment	25,000	20,000	−5,000
	Integrated testing and UAT support	20,000	20,000	0
	Documentation, training and knowledge transfer	15,000	15,000	0
	Implementation subtotal	**1,05,000**	**1,00,000**	**−5,000**
	Cross-module dependency coordination and project governance	10,000	10,000	0
	Complete ERP total (ex GST)	**4,80,000**	**3,80,000**	**−1,00,000**

Lines 1 to 14 and 17 (15 lines) each lose a ₹5,000 AI adapter, ₹75,000 in all; line 18 loses ₹5,000 of workflow automation; line 19 is removed; the adapter wiring in cross-module integration falls by ₹5,000. Dispatch and Contracts are unchanged: they are small, record-keeping modules priced for the module itself. Module numbers keep the enquiry's 19-line numbering, so line 19 stays visible as removed rather than renumbered.

Complete boundary. All 18 operating modules at the **agreed baseline depth**: standard workflows and limited customisation. The detailed specification and module acceptance criteria fix that baseline before development starts. Explicitly outside it: any AI or AI adapter, escalation rules, cross-module triggers and auto-generated documents, bulk historical data migration, statutory compliance certification, and any integration with third-party systems.

Price difference between the options: ₹1,40,000, so Option 2 costs about 58.3% more than Option 1 for the extra breadth. The MVP is roughly 55% of the Complete ERP's functional scope (a planning estimate, not a measured figure) and is priced at about 63.2% of it, because the foundations (architecture, sign-in, permissions, numbering, deployment, testing, documentation) are needed in both.

06 MVP versus Complete, module by module

MODULE	OPTION 1: MVP	OPTION 2: COMPLETE
CRM	Customer records, enquiries, follow-ups	Full pipeline, RFQ and tender tracking, correspondence, complaints, advanced history
Project management	Projects, milestones, tasks, deadlines, status	Dependencies, WBS, budgets, risk and change management, advanced reporting
Enquiry, quotation, sales	Quotations, basic costing, revisions, order confirmation	Advanced costing, alternative offers, PO comparison, sales orders, retention, LDs, milestone billing
Engineering and PLM	Product and component records, BOMs, drawing attachments, revisions	Multi-level BOMs, engineering change orders, formal design approvals

MODULE	OPTION 1: MVP	OPTION 2: COMPLETE
Document management	Repository, numbering, revision history, search, basic approvals	Full controlled-document lifecycle, transmittals, acknowledgements, advanced audit and distribution
Manufacturing	Job cards, operation sequences, material allocation, status	Advanced routing, work-centre scheduling, labour tracking, WIP, subcontracting, bottleneck analytics
Travellers	Configurable travellers, checkpoints, sign-offs	BOM-driven travellers, QR codes, full genealogy, customer-facing formats
Quality	Incoming, in-process and final inspection, NCRs, quality release	QAP/ITP, CAPA, audits, calibration, supplier quality, analytics
Barcode, QR, traceability	Basic material and job references, manual tracking	Barcode scanning, batch, heat and serial tracking, product genealogy
Procurement	Suppliers, purchase requests, receipts, purchasing	Approval workflows, RFQs, comparative statements, supplier performance, subcontracting
Inventory	Stock balances, material issues, reservations, shortages	Multi-warehouse and bins, valuation, reconciliation, ageing, advanced traceability
Planning and MRP	Job priorities, manual material planning	Automated BOM-based MRP, capacity planning, scheduling, shortage recommendations
Testing and equipment	Basic test records and attachments	Dedicated test workflows, automated reports, calibration, preventive maintenance
Finance and accounting	None	Invoicing and payment status, GST support, reconciliation, receivables and payables, profitability, all inside Verity
HR and payroll	None	Employees, attendance, leave, payroll, statutory calculations, competency tracking
Dispatch	Delivery readiness tracking	Dispatch planning, packing lists, challans, shipment tracking, partial deliveries
Contracts and risk	Basic project and order references	Obligations, bank guarantees, LD exposure, insurance and NDA tracking, risk registers
Dashboards	Operational dashboards for the included workflows	Cross-department KPIs, profitability, ageing, cash flow, supplier and resource analytics
Notifications	Basic in-app reminders and alerts	Configurable approval workflows with in-app and e-mail reminders. DEFERRED escalations, cross-module triggers, automated documents
AI	NOT INCLUDED	NOT INCLUDED deferred; quoted on request (section 3)

Boundaries and acceptance for the higher-risk modules (Options 2 and 3)

The detailed specification fixes each module's depth in writing before development starts. These are the boundaries we will hold to.

AREA	INCLUDED AT THE AGREED DEPTH	EXCLUDED	ACCEPTED WHEN
Finance and accounting	Invoice records from orders and milestones, recorded payments and receipts, receivables and payables views, configurable GST rates, job profitability	GST return and portal filing, e-invoicing, bank feeds, statutory audit certification, multi-company consolidation	An invoice from an order shows tax and outstanding amount; a recorded payment reduces it; receivables reconcile to invoices and payments; job profitability reconciles to recorded costs
HR and payroll	Employee records, attendance, leave, shifts, timesheets, salary structures, payroll runs using statutory components configured from DSEW-supplied rules, payslips	Statutory filing and portal submission, legal compliance certification, attendance-device integration, rule changes DSEW has not configured	A sample month for agreed employees reproduces DSEW's own calculation using its supplied rules
Engineering and revisions	Product and component masters, multi-level BOMs, revisions with release, engineering change requests and orders with approval, drawing attachments	CAD integration or editing, simulation tools, 3D viewing	A released revision cannot be edited; an order records its revision; a change creates a new revision through approval
Quality workflows	Inspection plans, checklists and acceptance criteria, NCR and CAPA, calibration records, QAP/ITP templates for the agreed formats, approvals inside the system	Customer formats beyond the agreed number, drafting of quality manuals, accreditation or certification work	A failed or missing mandatory check blocks release; an NCR closes only after CAPA verification
Workflows and notifications	Configurable approval steps and conditions, who drafts, reviews, approves and releases, in-app and e-mail reminders	Escalation chains, cross-module triggers, automatic document generation	An approval above a configured value routes to the configured approver; a self-approval attempt is refused where the rule forbids it
AI	None in this edition	Any AI feature, adapter, model, index or hardware	Not applicable; added only by written change request
Integrations	Everything is inside Verity; e-mail notifications through DSEW's mail server details	Any third-party or external system, WhatsApp, e-way bill, bank, GST portal, attendance devices; barcode scanner and printer hardware	Not applicable; added only by written change request

07 Option 3: the Complete ERP in four phases

PHASE	CONTENT	PREVIOUS (₹)	RECALCULATED (₹, EX GST)
1. Foundation and commercial core	Requirements and architecture, sign-in and roles, CRM, quotation and sales order, projects, document numbering, initial engineering masters and BOM	1,20,000	1,05,000
2. Supply chain and manufacturing core	Engineering revisions and release, procurement, inventory and material allocation, planning and basic MRP, manufacturing jobs and operations	1,35,000	1,10,000
3. Quality, traceability and operational controls	Travellers, quality and NCRs, barcode/QR and traceability, testing and equipment, dispatch, contracts and compliance	1,30,000	1,10,000
4. Business modules, validation and go-live	Finance and accounting, HR and payroll, dashboards, notifications and approval workflows, end-to-end testing, UAT, deployment, training, handover	95,000	55,000
Total	**About 8 to 12 weeks**	**4,80,000**	**3,80,000**

Each phase falls by the lines it contains: phase 1 by ₹15,000 (modules 1, 2, 4), phase 2 by ₹25,000 (3, 5, 9, 10, 11), phase 3 by ₹20,000 (6, 7, 8, 12), phase 4 by ₹40,000 (13, 14, 17, the ₹5,000 automation reduction in 18, the removed line 19 and the ₹5,000 integration reduction). Phase acceptance criteria are as in document 2, without the AI use cases. Phase prices allocate the Option 2 total; payments follow the milestones in section 8.

08 Payment

Each invoice is tied to its milestone, carries GST at the rate then applicable, and is **payable within 7 calendar days**. The same structure applies to Options 1, 2 and 3.

MILESTONE	SHARE	OPTION 1 (₹, EX GST)	OPTION 2 / 3 (₹, EX GST)
1. Kickoff: signed order, product owner named, requirements signed off	30%	72,000	1,14,000
2. Core workflow demonstration accepted: the commercial core and first working release	30%	72,000	1,14,000
3. Integrated testing and UAT build delivered to DSEW	30%	72,000	1,14,000
4. Handover and go-live: UAT signed off, go-live gates passed, handover signed	10%	24,000	38,000
Total	**100%**	**2,40,000**	**3,80,000**

Review window. DSEW has **5 business days** after each milestone delivery to report material deviations from the agreed criteria. In-scope defects are corrected before sign-off; new requirements follow change control. No report in the window means the milestone is accepted. The monthly testing period fee is invoiced separately (section 9).

GST at 18% is added to every fee: ₹43,200 on Option 1 and ₹68,400 on Option 2, illustrative. IGST is expected, as our GSTIN is registered in Delhi and DSEW is in Madhya Pradesh; the rate and head are confirmed at invoicing.

09 The testing period

Unchanged from the first proposal. After go-live, DSEW tests Verity in its real workflows for as many months as it chooses, for one bundled fee of **₹8,500 a month** ex GST, the same for either option. It starts on the go-live date (gates passed and handover signed), is invoiced monthly in advance, payable within 7 calendar days, and can be ended at the close of any monthly cycle by written notice before the next invoice date.

Defect warranty

Reproducible defects against the signed requirements are corrected, found in UAT or at any time during the testing period. Defects caused by DSEW's own changes, hardware, network or third-party software are not Verity defects.

Testing assistance

Help running the agreed UAT scripts and real jobs, reproducing and triaging each report, and reviewing feedback with DSEW at an agreed interval.

Routine maintenance

Tested releases, stability and security updates, help running and checking backups and restores, and administrator guidance.

Service terms. Remote support by email (team@plotarmour.in) and phone (+91 87440 69597), Monday to Saturday, 10:00 to 18:00 IST; up to 8 hours a month included; acknowledgement within 1 business day; a fix or workaround plan for a reproducible defect within 3 business days. Escalation: Shubhankar Rakshit, CFO. Not covered, and quoted separately with DSEW's written approval first: new features, changes to accepted requirements, additional integrations, new product families, reports, formats, users or sites, data cleansing or migration beyond the agreed imports, hardware and network faults, and on-site work and travel.

10 What the lower scope does to DSEW's server

Dropping AI removes the largest variable in the sizing. The core ERP VM stays at its original specification, and no AI tier, index or GPU machine is needed.

ITEM	FIRST PROPOSAL (WITH AI SEARCH)	RECALCULATED EDITION
VM processors	4 to 6 vCPU	4 vCPU (4 to 6 recommended headroom)
VM memory	32 GB, static	16 GB, static
Disk	500 GB mirrored SSD plus index space	500 GB mirrored SSD; document volume separate, sized with DSEW

ITEM	FIRST PROPOSAL (WITH AI SEARCH)	RECALCULATED EDITION
Background load	Report generation, file indexing and AI indexing as scheduled jobs	Report generation and file indexing as scheduled jobs; no AI indexing
Separate GPU workstation	About 16 GB GPU if interactive drafting is chosen	Not needed
Outbound data to a provider	Only if an external AI service is enabled	None by design; no AI service exists in the solution

DSEW's own costs are as in document 2 (planning estimates, not quotations): backup target and UPS ₹0.8 to 1.2 lakh; a new server only if the existing one cannot run the VM, ₹3.5 to 4.5 lakh; no platform software licences. The 4 vCPU, 16 GB RAM, 500 GB figure remains a design target confirmed at the pre-deployment survey and proven by a load test on DSEW's VM before go-live. No component in the solution is a paid third-party licence.

11 Cost over one, three and five years

If DSEW keeps the testing period running for every month shown (it may end it at any monthly cycle), the cumulative amount is as below, ex GST. Later enhancements are not priced.

HORIZON	TESTING PERIOD (₹)	OPTION 1 CUMULATIVE (₹)	OPTION 2 / 3 CUMULATIVE (₹)
At go-live	0	2,40,000	3,80,000
12 months	1,02,000	3,42,000	4,82,000
36 months	3,06,000	5,46,000	6,86,000
60 months	5,10,000	7,50,000	8,90,000

12 How this edition relates to documents 2 to 5

Documents 2 to 5 of the proposal package remain the reference for delivery, ownership, company and technical detail. Where they mention AI or automation, or price, this edition governs.

DOCUMENT	EFFECT OF THE RECALCULATED EDITION
1 Proposal	Prices, module tables, AI position, payment amounts and the AI-hardware discussion are superseded by this document
2 Delivery and deployment	Phase prices and the phase 4 content change as in section 7; "and AI may need more" in the hardware rows no longer applies; timelines, gates, environments, assumptions and the compatibility check are unchanged
3 Licence and ownership	Unchanged

DOCUMENT	EFFECT OF THE RECALCULATED EDITION
4 Company and platform	Unchanged, except that the "documented AI use cases" in the last capability row are not part of this edition
5 Technical solution	Sections 6 to 12 and 14 to 19 apply as written. Section 13 (AI options by hardware tier), section 7.6 (optional AI hardware) and the 32 GB "with AI search" column of section 7.1 are not part of this edition and are available only by change request

13 Where things stand, and what follows

Verity's foundations (data isolation, permissions, audit, stock, manufacturing orders, QC checkpoints, project jobs, approvals, QR identity) exist and have been run on our test environments with fictional data. Revision-controlled BOMs, controlled documents, structured test records, HR and payroll, finance and the other modules beyond the foundations are built during the project, which is why the timelines are ranges.

Before DSEW goes live, these gates are passed together with DSEW (document 2, section 6): the compatibility check on DSEW's host and Windows Server 2019, a real-phone HTTPS upload, a rehearsed combined restore of database, files and identity, and the outage tests. **Production use starts only after they pass.**

Next step: reply to team@plotarmour.in with the option you prefer and the name of the person who decides for DSEW, and we will send the kickoff date. We would be glad to walk through the recalculated scope on a call first.

This edition is valid for 60 days from 23 October 2026. The licence and ownership wording remains subject to legal review (document 3). PlotArmour, 31/44 St 3, Block 17, Vishwas Nagar, Delhi 110032 · GSTIN 07TQDPS9711L1ZT · team@plotarmour.in · +91 87440 69597.
